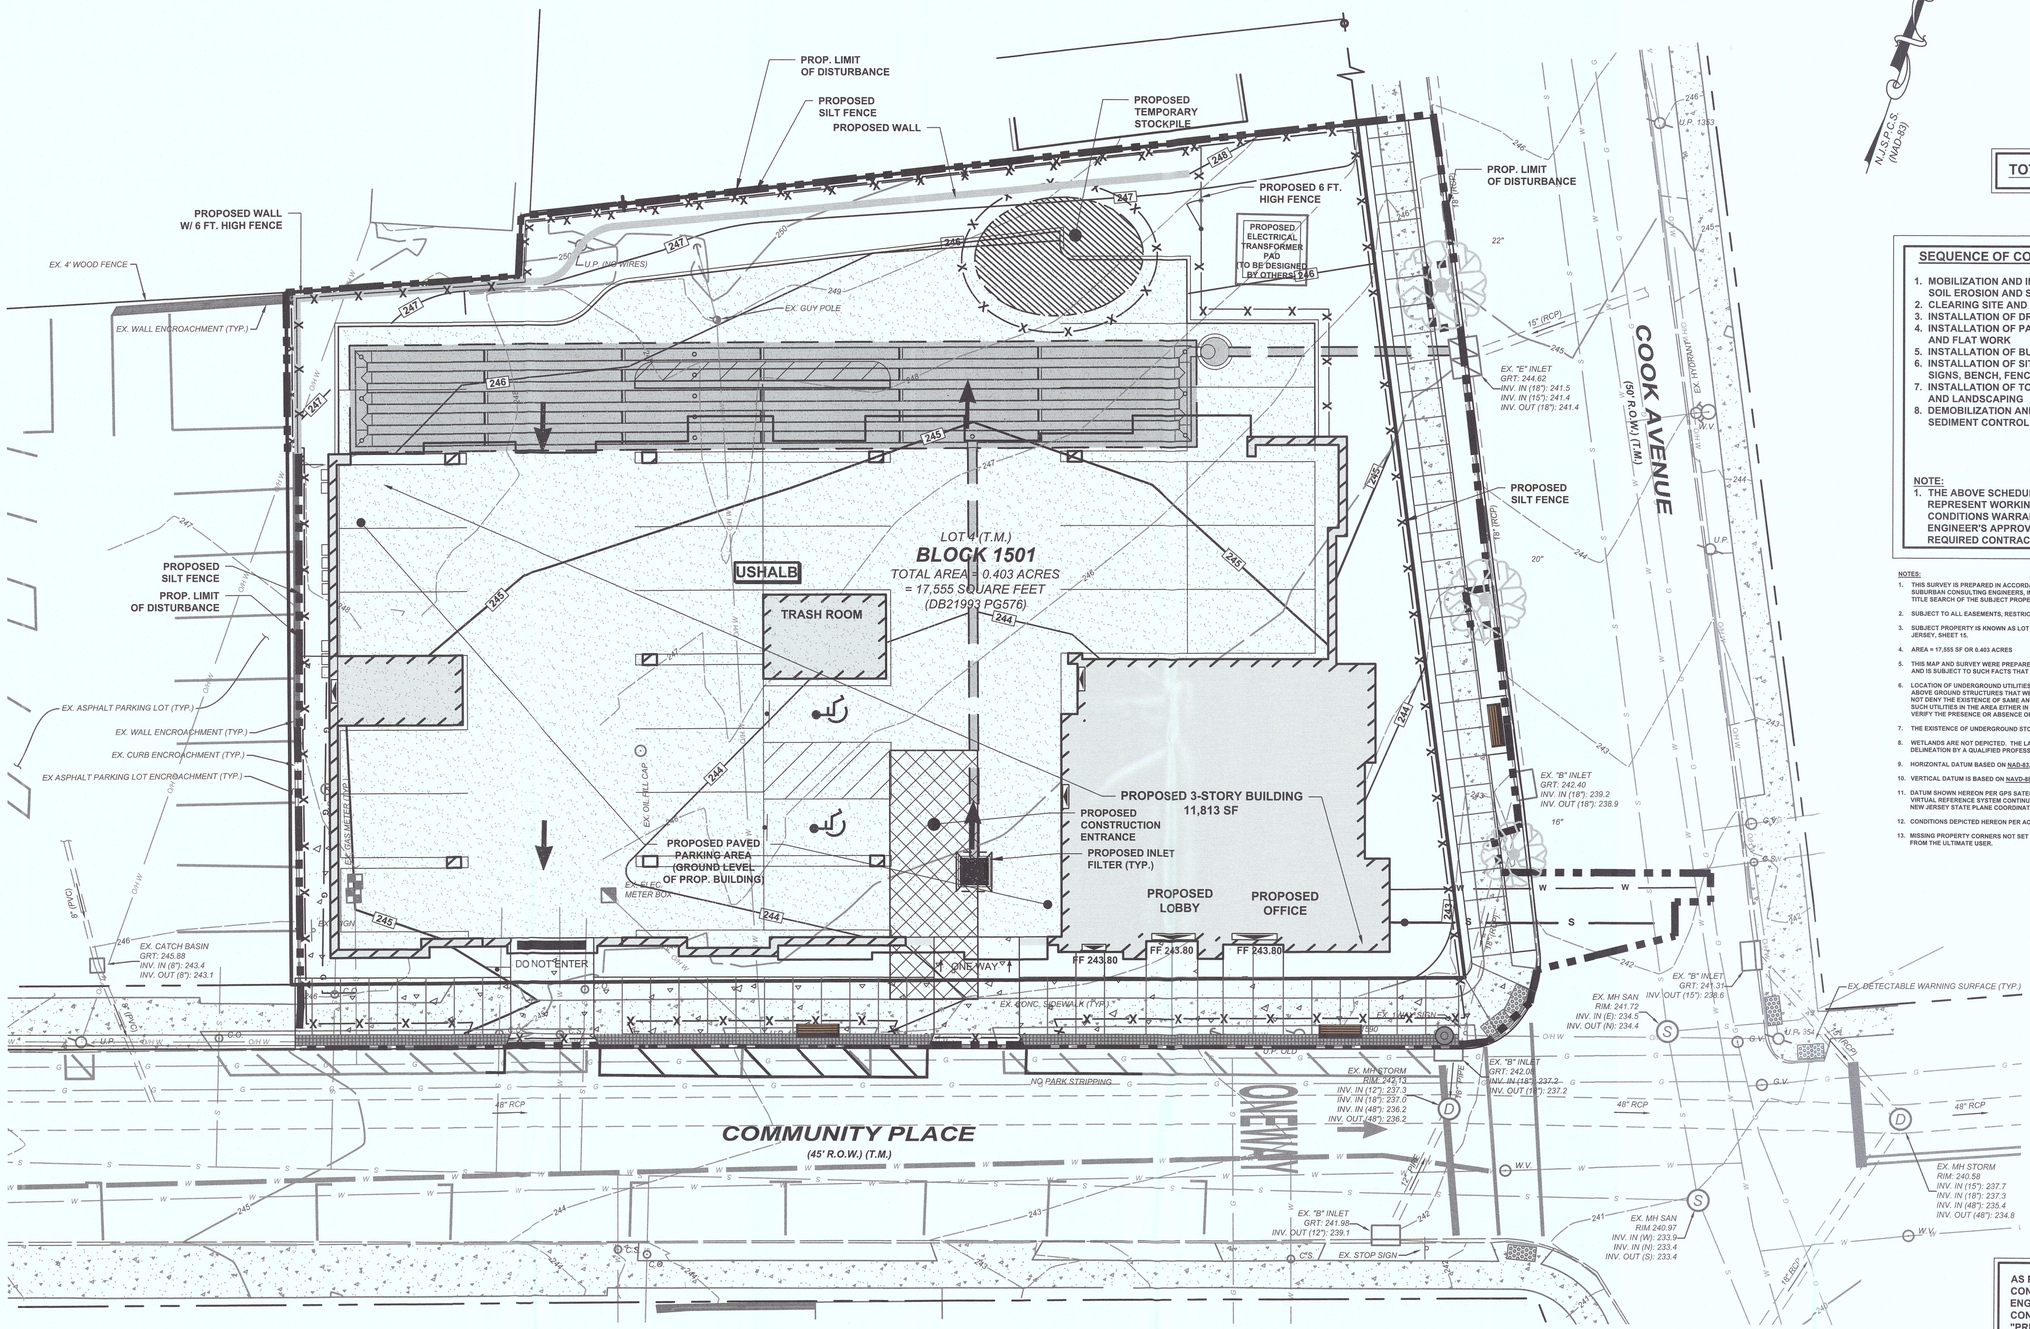

TOTAL DISTURBANCE = 20,468 S.F. (0.47 ACRES)

SEQUENCE OF CONSTRUCTION AND DURATION (8 MONTHS, 18 WEEKS)

1.	MOBILIZATION AND INSTALLATION OF SOIL EROSION AND SEDIMENT CONTROL MEASURES	1 WEEK
2.	CLEARING SITE AND DEMOLITION, EXCAVATION	5 WEEK
3.	INSTALLATION OF DRAINAGE STRUCTURES, PIPES, UTILITY MAINS	3 WEEK
4.	INSTALLATION OF PAVEMENT, APRONS, CONCRETE CURBS, AND FLAT WORK	2 WEEKS
5.	INSTALLATION OF BUILDING	8 MONTHS
6.	INSTALLATION OF SITE AMENITIES INCLUDING: SIGNS, BENCH, FENCE, WALL, ETC.	3 WEEKS
7.	INSTALLATION OF TOPSOIL, FERTILIZER, SEED AND MULCH, AND LANDSCAPING	3 WEEKS
8.	DEMOBILIZATION AND REMOVAL OF SOIL EROSION AND SEDIMENT CONTROL MEASURES	1 WEEK
	TOTAL:	8 MONTHS, 18 WEEKS

NOTE:
1. THE ABOVE SCHEDULE OF CONSTRUCTION ACTIVITIES ARE ESTIMATES THAT REPRESENT WORKING DAYS AND MAY VARY IN THE SEQUENCE AND DURATION AS CONDITIONS WARRANT. THE CONTRACTOR SHALL SUBMIT A SCHEDULE FOR THE ENGINEER'S APPROVAL AND MAKE PERIODIC ADJUSTMENTS NECESSARY TO MEET THE REQUIRED CONTRACT TIME.

NOTES:

1. THIS SURVEY IS PREPARED IN ACCORDANCE WITH DOCUMENTS SUPPLIED BY THE CLIENT AND SUPPLEMENTAL INFORMATION OBTAINED BY SUBURBAN CONSULTING ENGINEERS, INC. THROUGH LIMITED RECORDS RESEARCH. THE DOCUMENTS USED DO NOT REPRESENT A COMPLETE TITLE SEARCH OF THE SUBJECT PROPERTY AND MAY OR MAY NOT BE ALL THE RELEVANT TITLE DOCUMENTS FOR THE SUBJECT PROPERTY.
2. SUBJECT TO ALL EASEMENTS, RESTRICTIONS, RIGHTS OF WAY, AND EXCEPTIONS OF RECORD.
3. SUBJECT PROPERTY IS KNOWN AS LOT 4, BLOCK 1501 AS SHOWN ON THE TAX MAP OF THE BOROUGH OF MADISON, MORRIS COUNTY, NEW JERSEY, SHEET 15.
4. AREA = 17,555 SF OR 0.403 ACRES
5. THIS MAP AND SURVEY WERE PREPARED FROM INFORMATION FURNISHED AND/OR OBTAINED TOGETHER WITH EVIDENCE FOUND ON THE GROUND AND IS SUBJECT TO SUCH FACTS THAT AN ACCURATE TITLE SEARCH MAY REVEAL.
6. LOCATION OF UNDERGROUND UTILITIES, IF DEPICTED, ARE APPROXIMATE. ALL LOCATIONS AND SIZES ARE BASED ON UTILITY MARK-OUTS, ABOVE GROUND STRUCTURES THAT WERE VISIBLE AND ACCESSIBLE AT THE TIME OF THE SURVEY. THE LACK OF UTILITY INFORMATION DOES NOT DENY THE EXISTENCE OF SAME AND SUBURBAN CONSULTING ENGINEERS, INC. DOES NOT GUARANTEE THE UTILITIES SHOWN COMPRISE ALL SUCH UTILITIES IN THE AREA EITHER IN SERVICE OR ABANDONED. REFERENCE TO THE APPROPRIATE UTILITY AUTHORITY SHOULD BE MADE TO VERIFY THE PRESENCE OR ABSENCE OF UTILITIES.
7. THE EXISTENCE OF UNDERGROUND STORAGE TANKS, IF ANY, WAS NOT KNOWN AT THE TIME OF THE FIELD SURVEY.
8. WETLANDS ARE NOT DEPICTED. THE LACK OF WETLAND INFORMATION DOES NOT DENY THE EXISTENCE OF SAME. SITE REVIEW AND DELINEATION BY A QUALIFIED PROFESSIONAL IN SAME CAN BE LOCATED IF REQUIRED.
9. HORIZONTAL DATUM BASED ON NAD-83, PER GPS SATELLITE OBSERVATION.
10. VERTICAL DATUM IS BASED ON NAVD-88, PER GPS SATELLITE OBSERVATION.
11. DATUM SHOWN HEREON PER GPS SATELLITE OBSERVATION AND SOLUTIONS PROVIDED REAL TIME BY KEYNET GPS, INC. WHICH UTILIZES TRIMBLE VIRTUAL REFERENCE SYSTEM CONTINUALLY OPERATING HIGH PRECISION GNSS REFERENCE STATIONS. DATUM PROVIDED IS NAD 83 / NAVD 88 NEW JERSEY STATE PLANE COORDINATE SYSTEM, ZONE 2900.
12. CONDITIONS DEPICTED HEREON PER ACTUAL FIELD INSTRUMENT SURVEY PERFORMED MARCH 16, 2020.
13. MISSING PROPERTY CORNERS NOT SET AT THIS TIME, PER N.J.A.C. 13:40-5.2, A WRITTEN WAIVER OF CORNER MARKER(S) HAS BEEN OBTAINED FROM THE ULTIMATE USER.

REFERENCES:

1. *TAX MAP - LOT 4, BLOCK 1501, ON THE CURRENT TAX MAP OF THE BOROUGH OF MADISON, SHEET #15.*
2. *ORTHOPHOTOGRAPHY - NJ OFFICE OF INFORMATION TECHNOLOGY (NJOIT), OFFICE OF GEOGRAPHIC INFORMATION SYSTEMS (OGIS), AND U.S. GEOLOGICAL SURVEY, 20160224, NEW JERSEY 2015 HIGH RESOLUTION ORTHOPHOTOGRAPHY, NAD83(2011) NJ STATE PLANE FEET, M=SD TILES: NJOIT, OGIS, PO BOX 212, TRENTON, NJ, 08625-0212, US.*
3. *AERIAL IMAGERY - © NEARMAP US, INC. http://go.nearmap.com*
4. *SURVEY - PROJECT LOCATION SURVEY PERFORMED ON 03/16/2020 BY SUBURBAN CONSULTING ENGINEERS, INC. AND SUPPLIMENTED WITH THE PLAN ENTITLED "BOUNDARY AND TOPOGRAPHIC SURVEY" PREPARED BY SUBURBAN CONSULTING ENGINEERS, INC. SIGNED ON 03/24/2020 AND REVISED ON 03/31/2020.*
5. *RECORD DEED - FROM BRAIN DEBIASSE TO BUDDY, TIMMY AND BRIAN, LLC, DATED JANUARY 25, 2012, AND RECORDED IN THE MORRIS COUNTY CLERK'S OFFICE ON MARCH 12, 2012, IN DEED BOOK 21993, PAGE 578.*
6. *CONSTRUCTION PLANS - "2018 CDBG PROJECT, COMMUNITY PLACE RECONSTRUCTION WATER MAIN REPLACEMENT PLAN" PREPARED BY BOROUGH OF MADISON DEPARTMENT OF ENGINEERING (MADISON, NJ), DATED FEBRUARY 2019 (UNSIGNED).*

LEGEND

— — —	PROPOSED LIMIT OF DISTURBANCE
—X——X—	PROPOSED SILT FENCE
⊠	PROPOSED INLET FILTER
USHALB	SOIL TYPE

Map Unit Symbol	Map Unit Name
USHALB	Urban Land-Haledon Complex, 3 to 8 percent slopes

AS PER NEW JERSEY DEPARTMENT OF AGRICULTURE STATE SOIL CONSERVATION COMMITTEE, CHAPTER 251, PL 1975 AS AMENDED, ENGINEERING POLICIES - TECHNICAL BULLETIN, THIS PROJECT IS CONSIDERED A METROPOLITAN AREA (PA1) AND IS CONSIDERED A "PREVIOUSLY DEVELOPED" SITE. THEREFORE, THIS PROJECT IS EXEMPT FROM SOIL COMPACTION REMEDIATION MEASURES.

10 0 10 20 30

SCALE: 1"=10'

NOTICE

THIS DRAWING AND ALL INFORMATION CONTAINED HEREIN IS AUTHORIZED FOR USE ONLY BY THE PARTY FOR WHOM THE WORK WAS CONTRACTED OR TO WHOM IT IS CERTIFIED.

THIS DRAWING MAY NOT BE COPIED, REUSED, DISCLOSED, DISTRIBUTED, OR RELIED UPON FOR ANY OTHER PURPOSE WITHOUT THE WRITTEN CONSENT OF SUBURBAN CONSULTING ENGINEERS, INC.

PER N.J.A.C. ELECTRONIC SUBMISSIONS NOT CONTAINING A VALID DIGITAL SEAL OR PAPER COPIES NOT CONTAINING A RAISED SEAL ARE NOT ORIGINALS AND MAY HAVE BEEN ALTERED.

© COPYRIGHT 2020 SUBURBAN CONSULTING ENGINEERS, INC.™

ALL RIGHTS RESERVED

DESCRIPTION	NO.	DATE:	BY:	CHK:
REVISED PER RECEIVED COMMENTS	B	10/09/2020	KAK	CJS
REVISED PER RECEIVED COMMENTS	A	08/21/2020	KRD	CJS

REVISIONS

DRAWN BY: CVF 05/14/2020

CHECKED BY: CJS 05/14/2020

CHECKED BY:

DAREN J. PHIL, PE
NJ PROFESSIONAL ENGINEER
LICENSE NO: 24GE03610100

DATE: 05/14/2020

SUBURBAN CONSULTING ENGINEERS, INC.
COA NO.: 24GA28037500
FIRM NO: 24BU000042300
- Civil Engineers - Municipal Engineers
- Landscape Architects -
- Planners - Environmentalists - Land Surveyors -
96 US Highway 206, Suite 101, Flanders, N.J. 07836 - 973.398.1776
2430 Highway 34, Bldg. A Suite 1R, Wall, N.J. 08736 - 732.282.1776
EXCELLENCE ♦ ECONOMY ♦ ENVIRONMENT

PRELIMINARY AND FINAL MAJOR SITE PLAN FOR PARK VALLEY DEVELOPMENT
No. 4 COMMUNITY PLACE, BLOCK 1501 LOT 4
BOROUGH OF MADISON, COUNTY OF MORRIS, STATE OF NEW JERSEY

SOIL EROSION AND SEDIMENT CONTROL PLAN

PROJECT NUMBER: SCE-11521.011

SCALE: 1"=10'

SHEET 8 OF 11

REVISION B

E:\SCE\Madison\11521 Madison\11521.011 4 Community Place\Sheets\11521.011 08 Soil Erosion Sediment Control Plan.dwg Thu, Oct 08, 2020 - 11:55am kkemper SUBURBAN CONSULTING ENGINEERS, INC.
